Campus Event App

Start Date 8/10/2025

Expected End Date 11/12/2025

Project Stage

Closure


Total Deliverable 8

Total Activity 11


Total Risk 3

Total Change Request 2


Activity Timeline with Progress

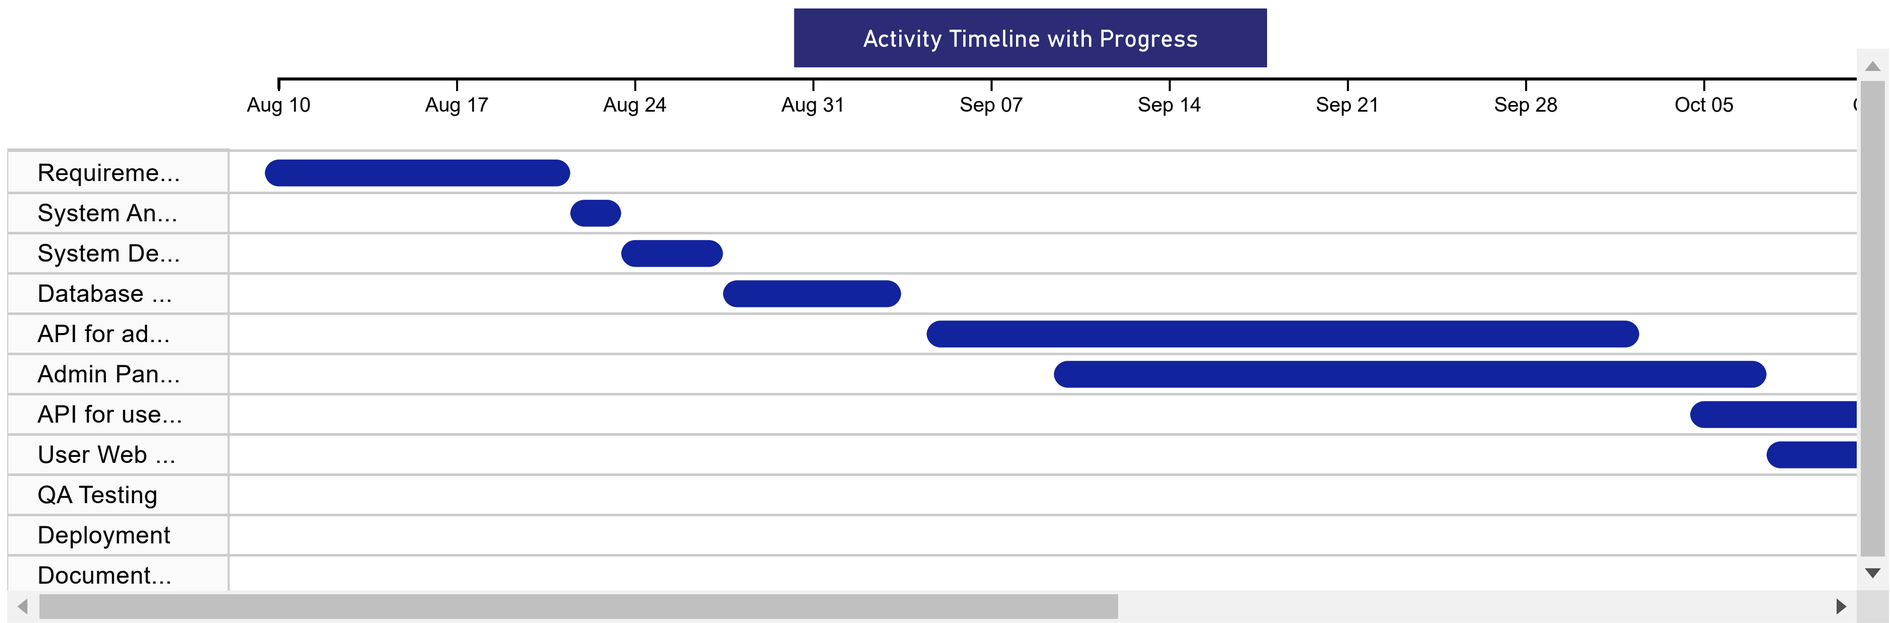

Key Metric

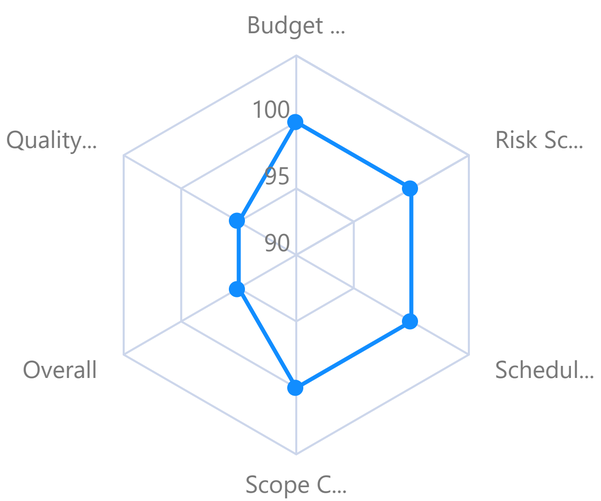

Quality Score

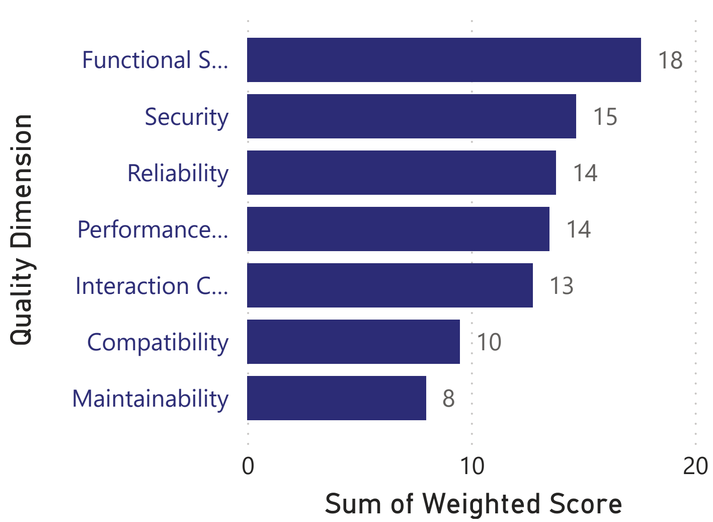

Project Triangle

Project Triangle	Baseline	Current	Variance %	Status
Cost (USD)	50000	41900	-0.16	Good
Scope (Activity)	11	11	0.00	Good
Time (Days)	104	102	-1.92	Good

Time Line Dashboard

Progress %

All

Total Deliverable

8


Total Activity

11

Total Activity Done 100%

11

Activity Timeline with Progress (Actual Plan)

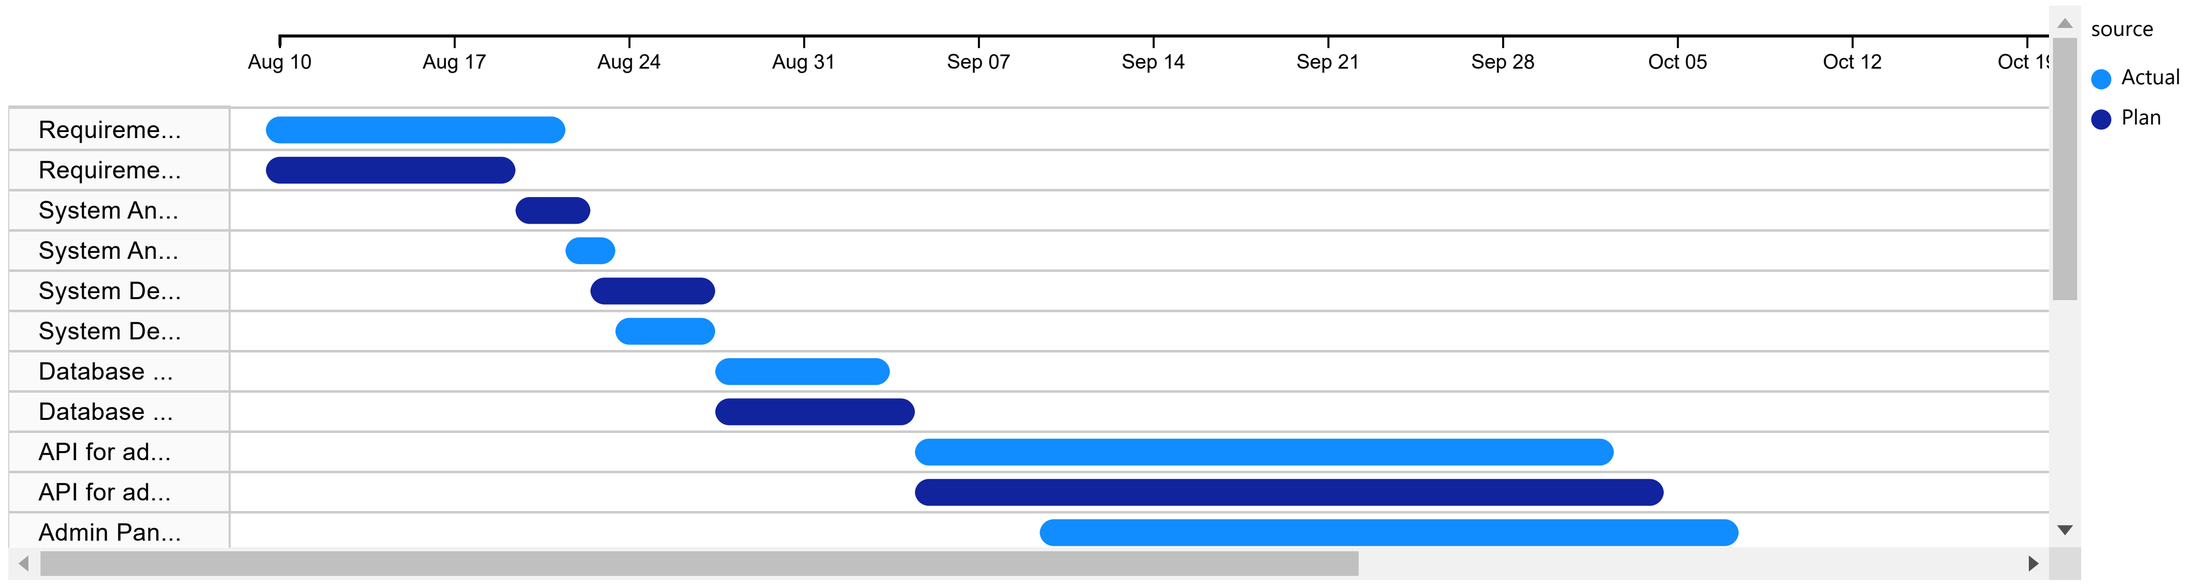

Activity WBS

Activity ID	Activity Name	Assigned To	Deliverable	Duration (days)	Resource	Dependen
A001	Requirements Gathering	BA Team	Requirements	10	BA	-
A002	System Analysis	Tech Lead	System Architecture	3	System Engineer	A001
A003	System Design	Tech Lead	System Architecture	5	System Engineer	A002
A004	Database Design	DBA	System Architecture	8	DBA	A002
A005	API for admin panel	Backend End Lead	Backend Module	30	dev	A004
A006	API for user web	Backend End Lead	Backend Module	20	dev	A004
A007	Admin Panel Development	Front End lead	Admin Panel	30	dev	A005
A008	User Web Development	Front End lead	User-web	20	dev	A006
A009	QA Testing	Tester	Testing	8	Tester	A005,A00

RACI Matrix

Activity / Task	Dev Team	Project Manager	QA Team	Sponser	System En
Admin Panel	A/R	C	C	I	I
Backend Module	A/R	C	C	I	I
Deployment	C	C	I	I	A/R
Documentation	I	R	I	A	I
Requirements	I	R	I	A	C
System Architecture	C	C	I	I	A/R
Testing	C	C	A/R	I	C
User-web	A/R	C	C	I	I

Time Line Dashboard

Resource vs Function Point

Component	Resource Planning	Function Point
Addational	$13,413	$13,413
Labor Cost	$36,125	$34,563
Total	**$49,538**	**$47,976**

Difference & Variance

Component	Difference	Variance %
Addational	0.00	0.00
Labor Cost	-1,562.50	-0.04
Total	**-1,562.50**	**-0.04**

Finalize

Higher Estimate:	Resource Planning
Difference:	1562.5
Recommendation:	Aligned (<10%)
Variance %:	0.031541761

Resource Allocation

Resource Type	Duration (month)	Quantity	Rate ($/month)	Sum of Total Cost ($)	Notes
Junior Dev	2.50	2	2000	10000	
PM	3.50	1	4000	14000	
QA Tester(Freelance)	0.25	1	3000	750	
Senior Dev	2.50	1	3500	8750	
System Engineer (Freelance)	0.50	1	3500	1750	Architet Design
System Engineer(Freelance)	0.25	1	3500	875	Deployment
Total				**36125**	

Function Point Cost Calculation

Activity	EI (×4)	EO (×5)	EQ (×4)	EIF (×5)	ILF (×7)	Effort (PM)	UFP	Productivity (FP/PM)	Rate ($/PM)	Sum of Labor Co
Admin Panel Development	8	6	0	0	0	7.75	62	8	500	
API for admin panel	0	4	6	0	0	5.50	44	8	500	
API for user web	0	5	3	0	0	4.63	37	8	500	
Database Design	0	0	0	0	7	6.13	49	8	500	
Deployment	0	0	6	0	8	10.00	80	8	500	
Documentation	0	0	0	0	6	5.25	42	8	500	
QA Testing	0	5	6	0	6	11.38	91	8	500	
Total										**3**

Addational cost

Cost Category	Amount ($)	qty/month	Sum of Total	Method	Notes
Cloud Hosting/Testing	30	10	300.00	Fixed	AWS, testing env
Contingency	3000	1	3,000.00	Fixed	Risk buffer
Hardware/Equipment	3000	1	3,000.00	Fixed	Laptops, servers
Software Licenses	2000	1	2,000.00	Fixed	Dev tools, IDEs
Training	1500	1	1,500.00	Fixed	Team training
Admin Overhead (20%)	7225	1	3,612.50	Percentage	20% of labor
Total			**13,412.50**		

Cost Spending Dashboard

Total Budget

50K


Total Spending

42K


Budget Left

8102


Spending Type

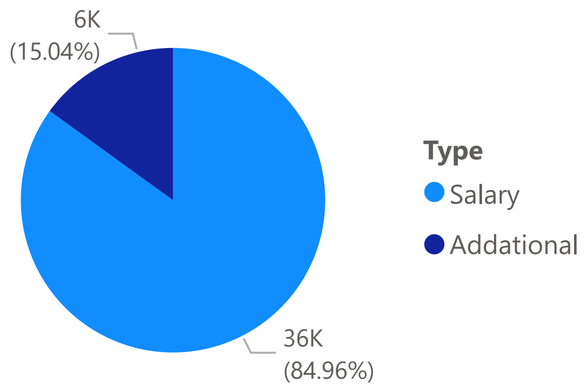

Budget Spending Trend

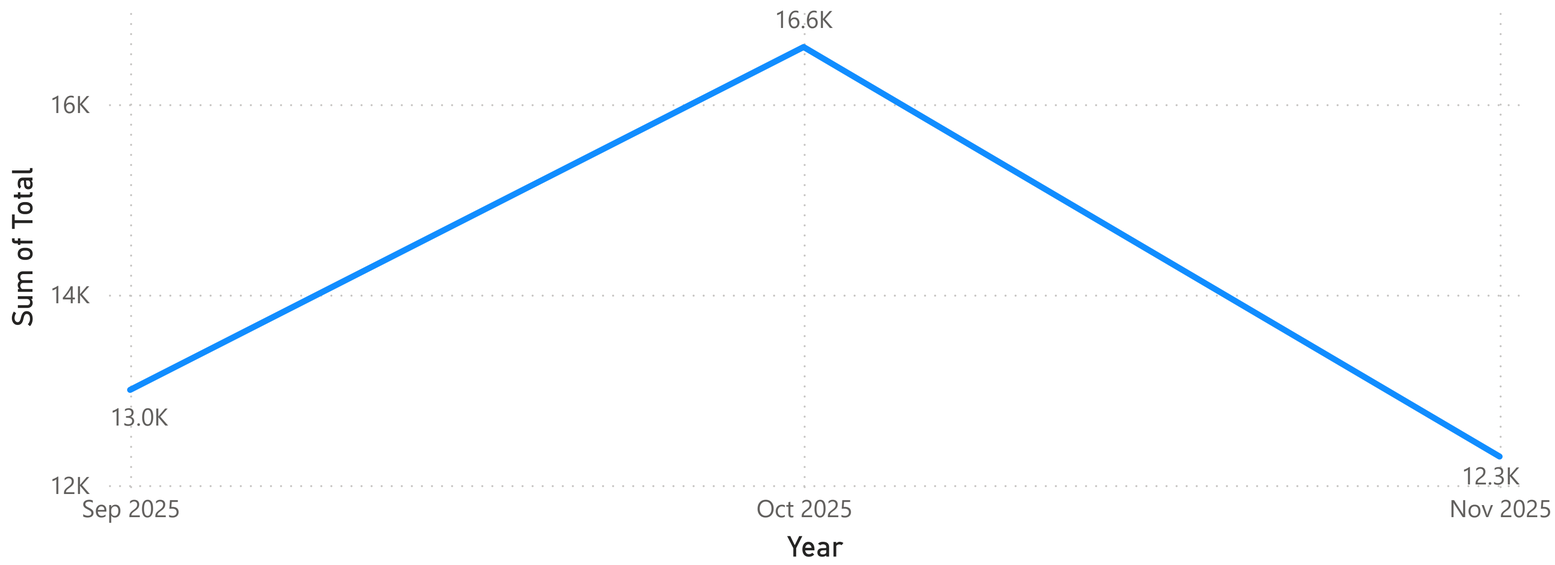

Spending Source

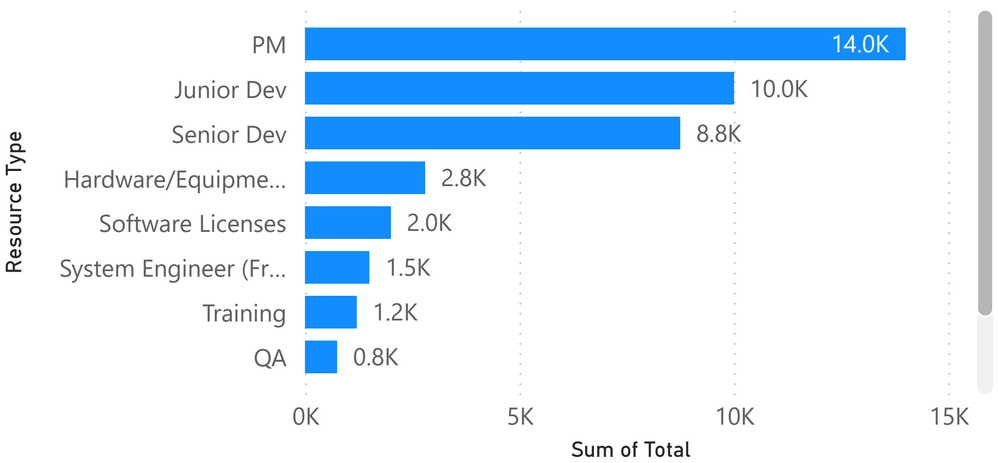

Budget Spending Details

Date	Type	Resource Type	Sum of Total	Notes
Friday, September 05, 2025	Salary	System Engineer (Freelance)	1500	
Wednesday, September 10, 2025	Salary	PM	4000	
Saturday, September 20, 2025	Salary	Junior Dev	4000	
Saturday, September 20, 2025	Salary	Senior Dev	3500	
Friday, October 10, 2025	Salary	PM	4000	
Monday, October 20, 2025	Salary	Junior Dev	4000	
Monday, October 20, 2025	Salary	Senior Dev	3500	
Tuesday, October 28, 2025	Addational	Hardware/Equipment	2800	Laptops, servers, "promotion 200"
Wednesday, October 29, 2025	Addational	Cloud Hosting/Testing	300	AWS, testing env
Total			**41900**	

Risks


Category: All

Urgency: All


Mitigation Plan: All

Status: All


Risk Category

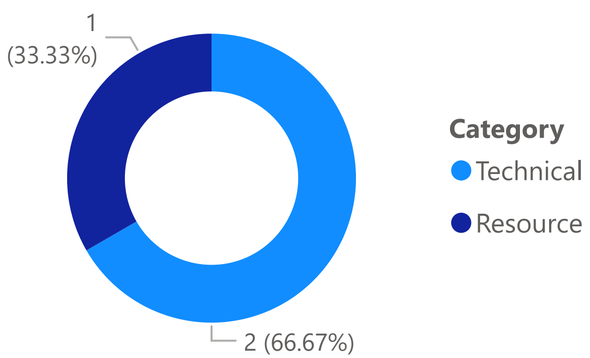


Risk Urgency

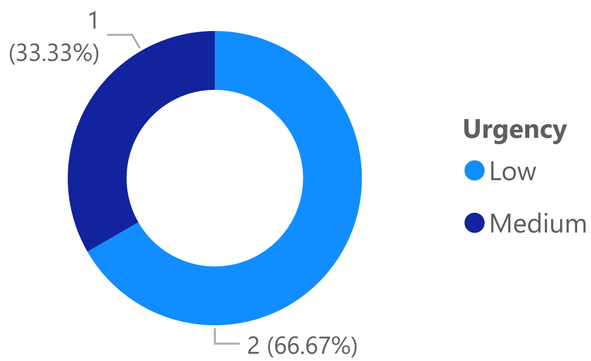

Risk Migration Plan

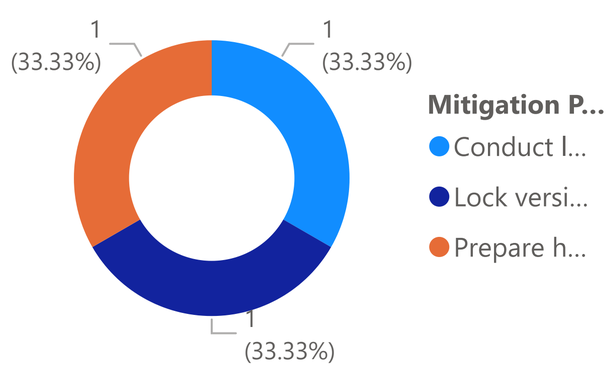

Risk Status



Risk Record

Risk ID	Risk Description	Category	Owner	Impact (1-5)	Probability (1-5)	Risk Score	Response Strategy	Status	Urgency	Mitigation Plan
R003	Lead developer might resign	Resource	PM	5	3	15	Mitigate	Solved	Medium	Prepare handover documents and contract
R004	UI framework update breaks compatibility	Technical	Dev Lead	3	4	12	Accepted	Solved	Low	Lock version and test compatibility
R005	Database performance issues at scale	Technical	System Analyst	4	2	8	Accepted	Solved	Low	Conduct load testing


Change Request

Request Date
8/28/2025 10/1/2025


Change Type
All

Risk Level
All


Change Request Type

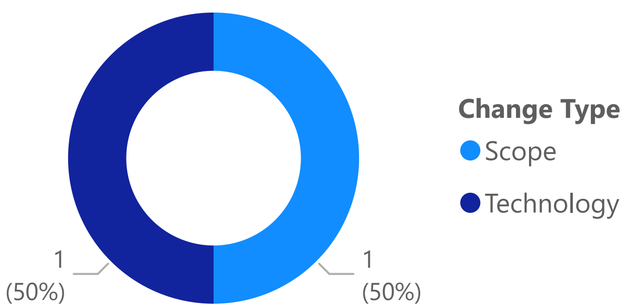

Change Request Risk Level

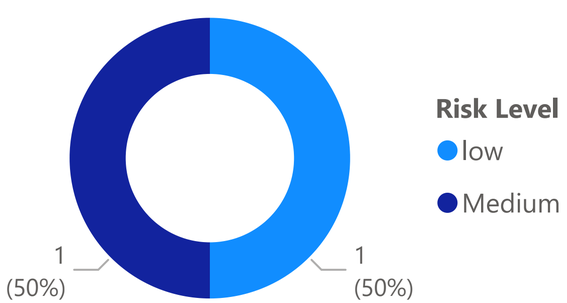

Change Request Trend

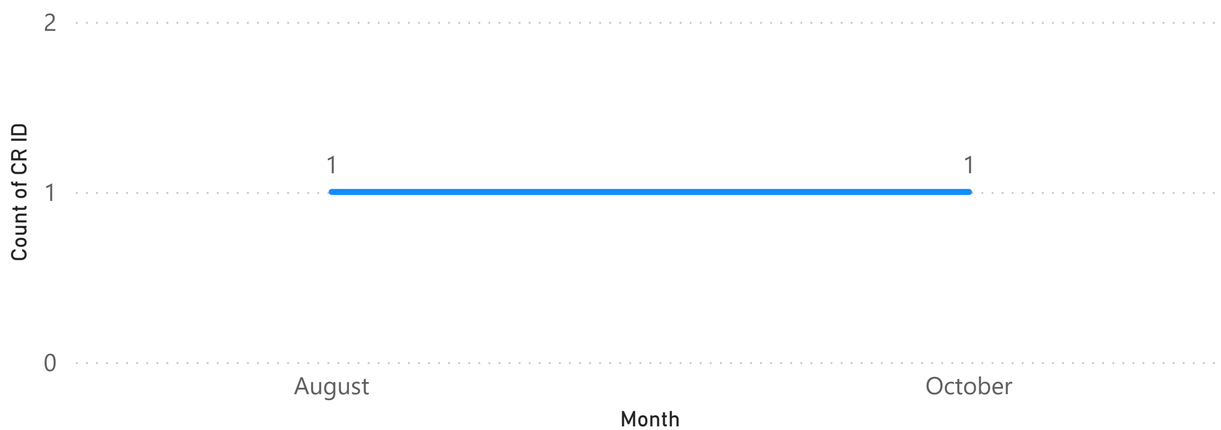

Change Requests

CR ID	Title	Change Type	Request Date	Decision Date	Request By	Approve By	Risk Level	Description
CR-01	Change Mysql to Postgresql	Technology	Thursday, August 28, 2025	Friday, August 29, 2025	System Architect	Dev lead/ PM	low	To use Postgresql Json data type support
CR-02	Include white and dark themes	Scope	Wednesday, October 01, 2025	Sunday, October 05, 2025	Sponser	Dev lead/ PM	Medium	Some user prefer to read in white while other prefer da

Stakeholder Dashboard

Stakeholder
All


Total Stakeholder

5


Total Meeting

24

Power and Interest Grid

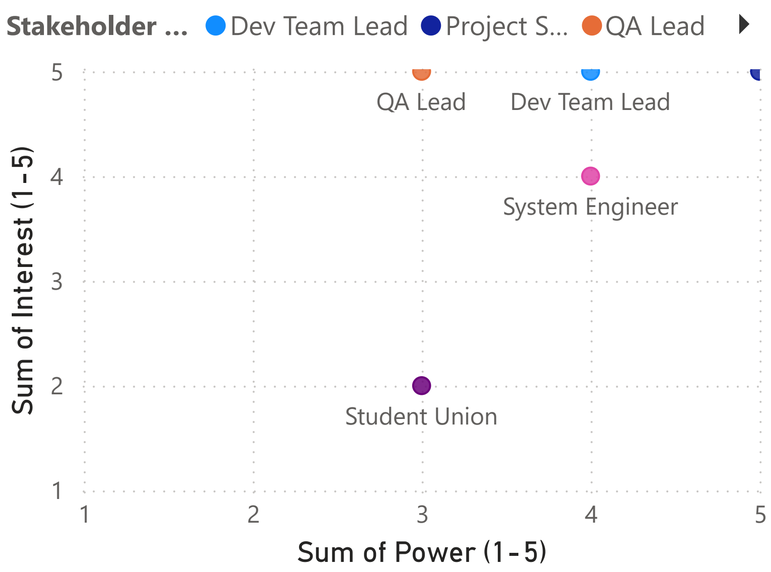

Meeting Trend

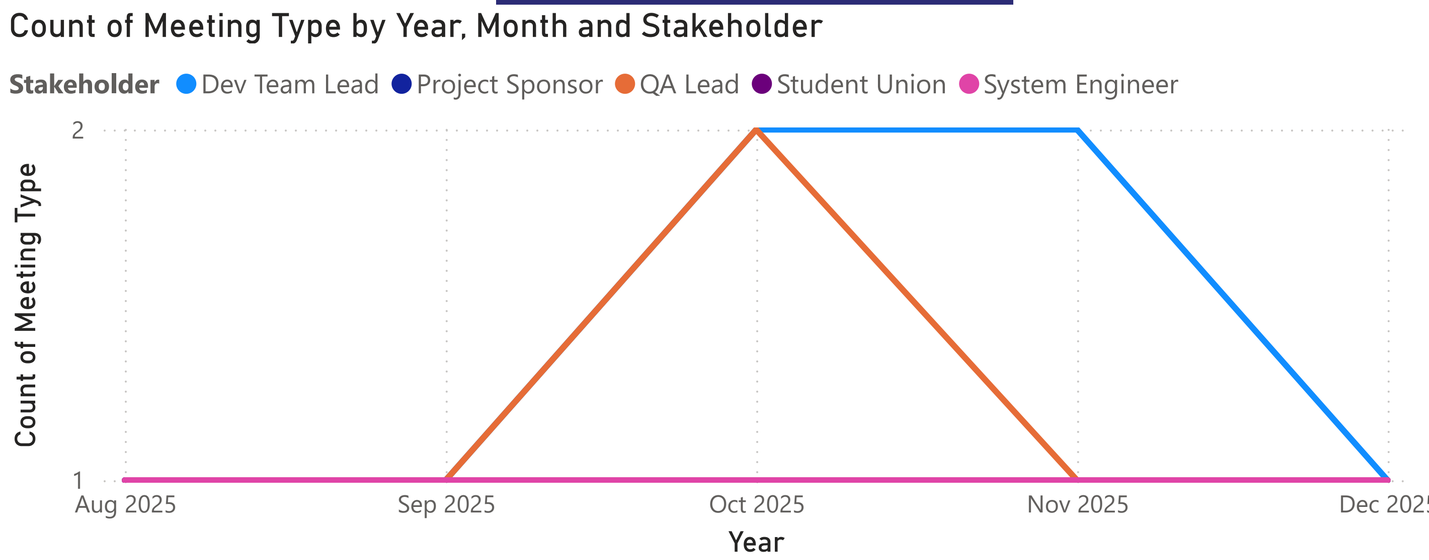

Communication Strategy

Audience/Stakeholder	Bi-weekly	Monthly	Weekly
Dev Team Lead			*
Project Sponsor		*	
QA Lead			*
Student Union		*	
System Engineer	*		

Emerging Strategy

Stakeholder Name/Role	Keep Informed	Manage Closely	Monitor
Dev Team Lead		*	
Project Sponsor		*	
QA Lead	*		
Student Union			*
System Engineer		*	

Meeting Log

Date	Stakeholder	Summary
Sunday, August 10, 2025	Project Sponsor	Confirmed scope, schedule, del
Tuesday, August 12, 2025	Student Union	Gathered initial user requireme
Wednesday, August 20, 2025	System Engineer	Agreed on server setup and DB
Friday, September 05, 2025	Dev Team Lead	API for admin panel started; no
Wednesday, September 10, 2025	QA Lead	Test plan drafted; waiting for m
Friday, September 12, 2025	Student Union	Validated early wireframes.
Monday, September 15, 2025	System Engineer	Staging DB functional; load test
Friday, October 03, 2025	Dev Team Lead	Admin Panel finished early; Use
Wednesday, October 08, 2025	QA Lead	Test cases ready for User Web.
